

	(A)	Name	Duration	Start	Finish	Predecessors
1	□	Projektstart	0.25 days	11/1/17 8:00 AM	11/1/17 10:00 AM	
		Johannes Hamfler	0.25 days	11/1/17 8:00 AM	11/1/17 10:00 AM	
		Oliver Friedrich	0.25 days	11/1/17 8:00 AM	11/1/17 10:00 AM	
		Ferdinand Malcher	0.25 days	11/1/17 8:00 AM	11/1/17 10:00 AM	
		Michal Frank	0.25 days	11/1/17 8:00 AM	11/1/17 10:00 AM	
2	✓	Anforderungsanalyse	5 days	11/1/17 10:00 AM	11/8/17 10:00 AM	1
		Johannes Hamfler	5 days	11/1/17 10:00 AM	11/8/17 10:00 AM	
		Oliver Friedrich	5 days	11/1/17 10:00 AM	11/8/17 10:00 AM	
3	V	Technologierecherche	5 days	11/8/17 10:00 AM	11/15/17 10:00 AM	2
		Johannes Hamfler	5 days	11/8/17 10:00 AM	11/15/17 10:00 AM	
		Oliver Friedrich	5 days	11/8/17 10:00 AM	11/15/17 10:00 AM	
4		Softwaredesign	20 days	11/15/17 10:00 AM	12/13/17 10:00 AM	0:00 AM (0:00 AM (0:0
5		Schnittstellenbeschreibung	10 days	11/15/17 10:00 AM	11/29/17 10:00 AM	3
		Oliver Friedrich	10 days	11/15/17 10:00 AM	11/29/17 10:00 AM	
6		Datenmodell	10 days	11/29/17 10:00 AM	12/13/17 10:00 AM	5
		Johannes Hamfler	10 days	11/29/17 10:00 AM	12/13/17 10:00 AM	
7	Ö	Abnahme Konzept	0.25 days	1/4/18 8:00 AM	1/4/18 10:00 AM	
		Johannes Hamfler	0.25 days	1/4/18 8:00 AM	1/4/18 10:00 AM	
		Oliver Friedrich	0.25 days	1/4/18 8:00 AM	1/4/18 10:00 AM	
		Ferdinand Malcher	0.25 days	1/4/18 8:00 AM	1/4/18 10:00 AM	
		Michal Frank	0.25 days	1/4/18 8:00 AM	1/4/18 10:00 AM	
8	V	Aufbau Entwicklungsumgebung	3 days	11/15/17 10:00 AM	11/20/17 10:00 AM	3
9	Ö	Implementierung	65 days?	1/1/18 8:00 AM	3/30/18 5:00 PM	2
1 0		Backend	7.5 days	1/1/18 8:00 AM	1/10/18 1:00 PM	
		Johannes Hamfler	7.5 days	1/1/18 8:00 AM	1/10/18 1:00 PM	
		Oliver Friedrich	7.5 days	1/1/18 8:00 AM	1/10/18 1:00 PM	
11		Frontend	7.5 days	1/10/18 1:00 PM	1/19/18 5:00 PM	3 4
		Johannes Hamfler	7.5 days	1/10/18 1:00 PM	1/19/18 5:00 PM	
		Oliver Friedrich	7.5 days	1/10/18 1:00 PM	1/19/18 5:00 PM	
1 2		Tests		1/22/18 8:00 AM	1/24/18 1:00 PM	11
		Johannes Hamfler	2.5 days	1/22/18 8:00 AM	1/24/18 1:00 PM	
		Oliver Friedrich	2.5 days	1/22/18 8:00 AM	1/24/18 1:00 PM	
1 3		Abnahme Prototyp 1	0.25 days	2/28/18 8:00 AM	2/28/18 10:00 AM	
		Johannes Hamfler	0.25 days	2/28/18 8:00 AM	2/28/18 10:00 AM	

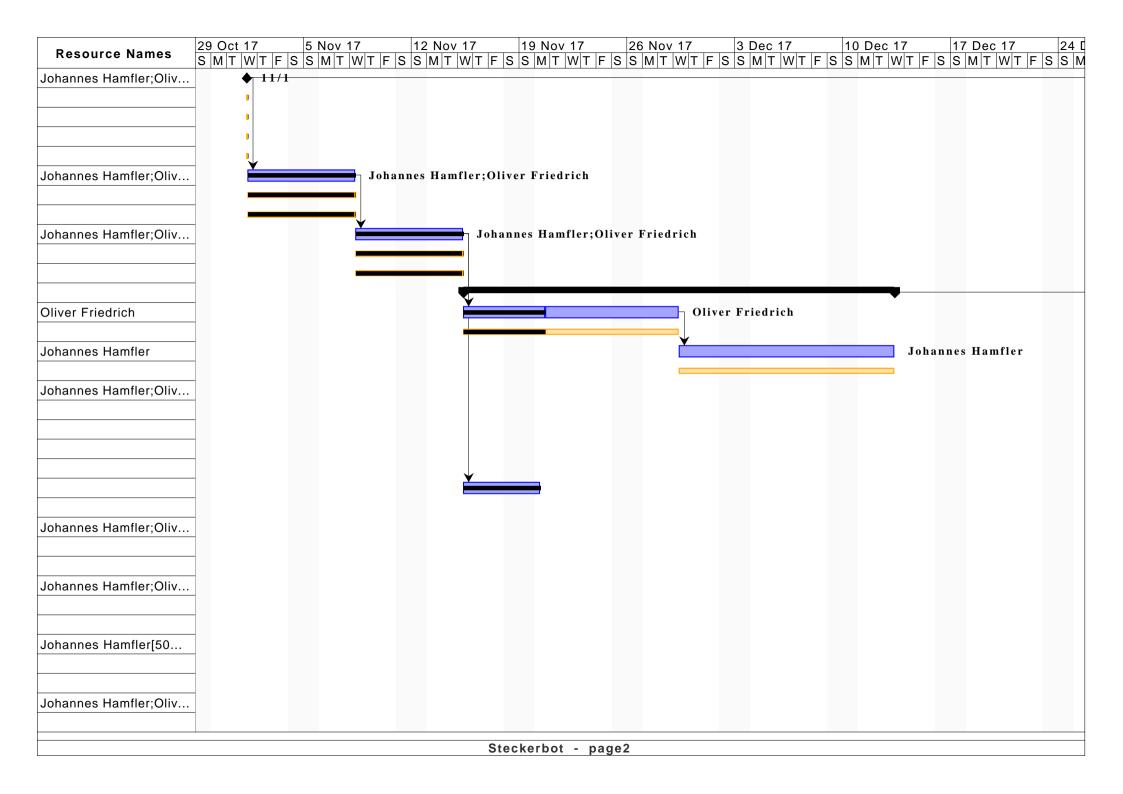

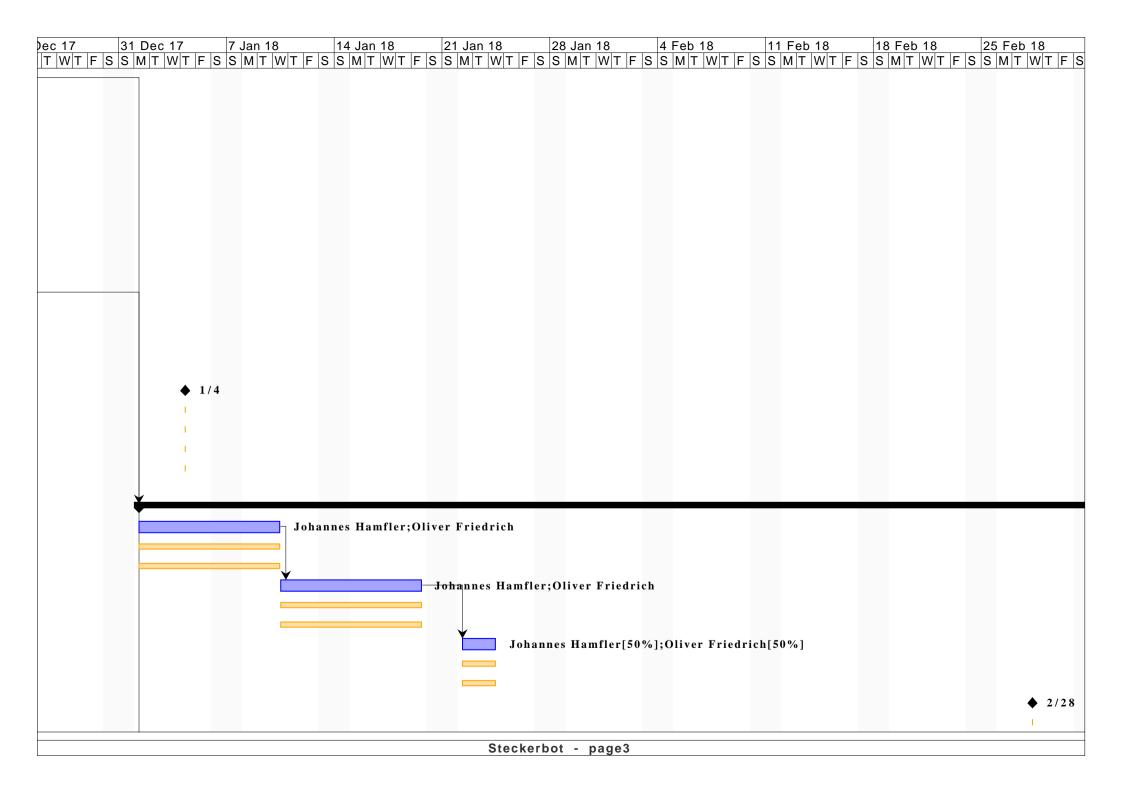

4 Mar 18 11 I	Mar 18 18 Mar 18	25 Mar 18 1 Apr 18	8 Apr 18 15 Apr 18 F S S M T W T F S S M T W T F	22 Apr 18 29					
	M T W T F S S M T W T F	S S M T W T F S S M T W T F	F S S M T W T F S S M T W T F	F S S M T W T F S S					
Steckerbot - page4									

	(B)	Name	Duration	Start	Finish	Predecessors
		Oliver Friedrich	0.25 days	2/28/18 8:00 AM	2/28/18 10:00 AM	
		Ferdinand Malcher	0.25 days	2/28/18 8:00 AM	2/28/18 10:00 AM	
		Michal Frank	0.25 days	2/28/18 8:00 AM	2/28/18 10:00 AM	
14		Implementierung der Änderungs	0.5 days?	1/1/18 8:00 AM	1/1/18 1:00 PM	
		Johannes Hamfler	0.5 days	1/1/18 8:00 AM	1/1/18 1:00 PM	
		Oliver Friedrich	0.5 days	1/1/18 8:00 AM	1/1/18 1:00 PM	
15	Ö	Abnahme Prototyp 2	0.333 days	3/28/18 7:00 AM	3/28/18 10:40 AM	
		Johannes Hamfler	0.333 days	3/28/18 7:00 AM	3/28/18 10:40 AM	
		Oliver Friedrich	0.333 days	3/28/18 7:00 AM	3/28/18 10:40 AM	
		Ferdinand Malcher	0.333 days	3/28/18 7:00 AM	3/28/18 10:40 AM	
16	Ö	Dokumentation	65 days	1/1/18 8:00 AM	3/30/18 5:00 PM	1
16		Johannes Hamfler	65 days	1/1/18 8:00 AM	3/30/18 5:00 PM	
		Oliver Friedrich	65 days	1/1/18 8:00 AM	3/30/18 5:00 PM	
17	Ö	Projektabschluss	4.5 days	3/30/18 10:00 AM	3/30/18 5:00 PM	16FS+3 days
		Johannes Hamfler	0.75 days	4/5/18 8:00 AM	4/5/18 3:00 PM	
		Oliver Friedrich	0.75 days	4/5/18 8:00 AM	4/5/18 3:00 PM	
		Ferdinand Malcher	0.75 days	4/5/18 8:00 AM	4/5/18 3:00 PM	
		Michal Frank	0.75 days	4/5/18 8:00 AM	4/5/18 3:00 PM	

Dagawaa Namaa	29 Oct 17	5 Nov	v 17	12 N	ov 17	19	Nov 17	26	Nov 17	3	Dec 17	10 Dec 17	1	7 Dec 17	24 [
Resource Names	29 Oct 17 S M T W T F	S S M	TWTF	S S M	T WT F	SS	M T W T F	SS	M T W T F	S S	M T W T F	S S M T W	T F S S	M T WT	F S S M
Johannes Hamfler;Oliv															
Johannes Hamfler;Oliv	_														
Jonannes Hanner, Onv															
Johannes Hamfler;Oliv															
Johannes Hamfler;Oliv															
					Q+.	acks	rbot - pa	200							

